

Appendix 3- LDP Timetables

Original Timetable- June 2016

- Approved by Planning Committee on 15 March 2016
- Approved by Full Council on 4 April 2016.
- The timetable was submitted to DFI/PAC on 11 April 2016 for agreement.
- The timetable was approved by DFI/PAC on 11 May 2016.

Belfast City Local Development Plan (LDP) 2035 - Timetable			
	Key Stages	Notes on Proposed Process	Indicative Timescales
Preliminary Work	Publication of Statement of Community Involvement (SCI)	<ul style="list-style-type: none"> • Final SCI to be submitted to Department for approval 	April 2016
	Publication of Timetable	<ul style="list-style-type: none"> • Consult Statutory Stakeholders • Final SCI to be submitted to Department for approval 	May 2016
	Preparation of evidence base to underpin production of Plan Strategy and Local Policies Plan	<ul style="list-style-type: none"> • Commission specific, specialist studies required (e.g. Population and Housing Growth) • Internal Council consultation to develop evidence base and identify key issues • Identification of key issues in relation to specific themes for consultation with relevant statutory consultees and key stakeholders • Consult consultation body (DAERA) with Sustainability Appraisal (incorporating SEA) Scoping Report 	May – June 2016
	Informal consultation with Elected Members, statutory stakeholders and community representatives		
	Publication of Preferred Options Paper	<ul style="list-style-type: none"> • 12 week public consultation • Publish Topic Papers and supporting evidence alongside POP, including appraisal of alternative options • Publication of Sustainability Appraisal (inc. SEA) Interim Report • Initial EqlA and HRA Screening 	September – November 2016
Plan Strategy	Consideration of responses to POP consultation	<ul style="list-style-type: none"> • Preparation of Public Consultation Report • Informal consultation with key stakeholders 	Early 2017
	Publication of Draft Plan Strategy	<ul style="list-style-type: none"> • 12 week public consultation, followed by 12 week consultation on representations • Publication of Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of EqlA and HRA where required 	Second half 2017
	Soundness Based Independent Examination	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Spring 2018
	Adoption of Plan Strategy	<ul style="list-style-type: none"> • Changes made to finalise Plan Strategy • Publication of final Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of final EqlA and HRA where required 	Early 2019*
Local Policies Plan	Informal consultation with Elected Members and statutory stakeholders	<ul style="list-style-type: none"> • Informal consultation with relevant statutory consultees and key stakeholders • Consult consultation body (DAERA) with Sustainability Appraisal (incorporating SEA) Scoping Report 	Spring 2018 – Early 2019
	Publication of Draft Local Policies Plan	<ul style="list-style-type: none"> • 12 week public consultation, followed by 12 week consultation on representations • Publication of final Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of final EqlA and HRA where required 	Spring - Autumn 2019
	Soundness Based Independent Examination	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Early 2020
	Adoption of Local Policies Plan	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Late 2020*
Monitor and Review	Monitoring and Review of LDP, including: <ul style="list-style-type: none"> • Annual Monitoring Reports • 5 and 10 year review (leading to commencement of a replacement Local Development Plan) 	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	On going

Sustainability Appraisal (incorporating Strategic Environmental Assessment (SEA))

* May require a longer period depending on changes required following Independent Examination

The First revised timetable- March 2018

The council sought to revise the original timetable as the existing work programme had exceeded due to the carrying out of additional complex pieces of work. In addition the council was advised by the PAC that the IE, at both formal stages, could take approximately one year and this has further implications for the current approved LDP timetable.

- Approved by Planning Committee on 14 November 2017.
- Approved by Full Council on 4 December 2017.
- The timetable was submitted to DFI/PAC on 21 March 2018 for agreement.
- The timetable was agreed by the DFI/PAC on 29 March 2018.

Belfast Local Development Plan (LDP) 2035 Timetable			
	Key Stages	Notes on Proposed Process	Indicative Timescales
Data Collection	Publication of Statement of Community Involvement (SCI)	<ul style="list-style-type: none"> • Final SCI to be submitted to Department for approval 	April 2016
	Publication of Timetable	<ul style="list-style-type: none"> • Consult Statutory Stakeholders • Final Timetable to be submitted to Department for approval 	May 2016
	Preparation of evidence base to underpin production of Plan Strategy and Local Policies Plan	<ul style="list-style-type: none"> • Commission specific, specialist studies required (e.g. Population and Housing Growth) • Internal Council consultation to develop evidence base and identify key issues • Identification of key issues in relation to specific themes for consultation with relevant statutory consultees and key stakeholders • Consult consultation body (DAERA) with Sustainability Appraisal (incorporating SEA) Scoping Report 	June – December 2016
	Informal consultation with Elected Members, statutory stakeholders and community representatives		
	Publication of Preferred Options Paper	<ul style="list-style-type: none"> • 12 week public consultation • Publish Topic Papers and supporting evidence alongside POP, including appraisal of alternative options • Publication of Sustainability Appraisal (inc. SEA) Interim Report • Initial EqlA and HRA Screening 	January - April 2017
Plan Strategy	Consideration of responses to POP consultation, develop evidence base engagement with key stakeholders and drafting of policies	<ul style="list-style-type: none"> • Preparation of Public Consultation Report • Informal consultation with key stakeholders 	May 2017 – March 2018
	Publication of Draft Plan Strategy	<ul style="list-style-type: none"> • Publish for viewing (4 weeks) • 8 week statutory public consultation, followed by 8 week statutory consultation on representations • Publication of Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of EqlA and HRA where required 	Spring – Autumn 2018
	Soundness Based Independent Examination	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Late 2018
	Adoption of Plan Strategy	<ul style="list-style-type: none"> • Changes made to finalise Plan Strategy • Publication of final Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of final EqlA and HRA where required 	Late 2019*
Local Policies Plan	Informal consultation with Elected Members and statutory stakeholders	<ul style="list-style-type: none"> • Informal consultation with relevant statutory consultees and key stakeholders • Consult consultation body (DAERA) with Sustainability Appraisal (incorporating SEA) Scoping Report 	Late 2018 – Early 2020
	Publication of Draft Local Policies Plan	<ul style="list-style-type: none"> • Publish for viewing (4 weeks) • 8 week statutory public consultation, followed by 8 week statutory consultation on representations • Publication of final Sustainability Appraisal (inc. SEA) and Public Consultation Report • Publication of final EqlA and HRA where required 	Spring - Autumn 2020
	Soundness Based Independent Examination	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Late 2020
	Adoption of Local Policies Plan	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	Late 2021*
Monitor and Review	Monitoring and Review of LDP, including: <ul style="list-style-type: none"> • Annual Monitoring Reports • 5 and 10 year review (leading to commencement of a replacement Local Development Plan) 	<ul style="list-style-type: none"> • Advisory report to Central Government • Central Government Issues binding report to Council 	On going


Sustainability Appraisal (incorporating Strategic Environmental Assessment (SEA))

* May require a longer period depending on changes required following Independent Examination

The second revised timetable- November 2018

The council sought for a second revision to the timetable as the revised launch date of the DPS and the immediate tasks in the process caused a delay and therefore was expected to expire over the proposed timeframe.

- Approved by Planning Committee on 11 September 2018.
- Approved by Full Council on 1 October 2018.
- The timetable was sent to DFI/PAC on 10 October 2018 for agreement.
- The timetable was agreed by DFI/PAC on 15 November 2018.

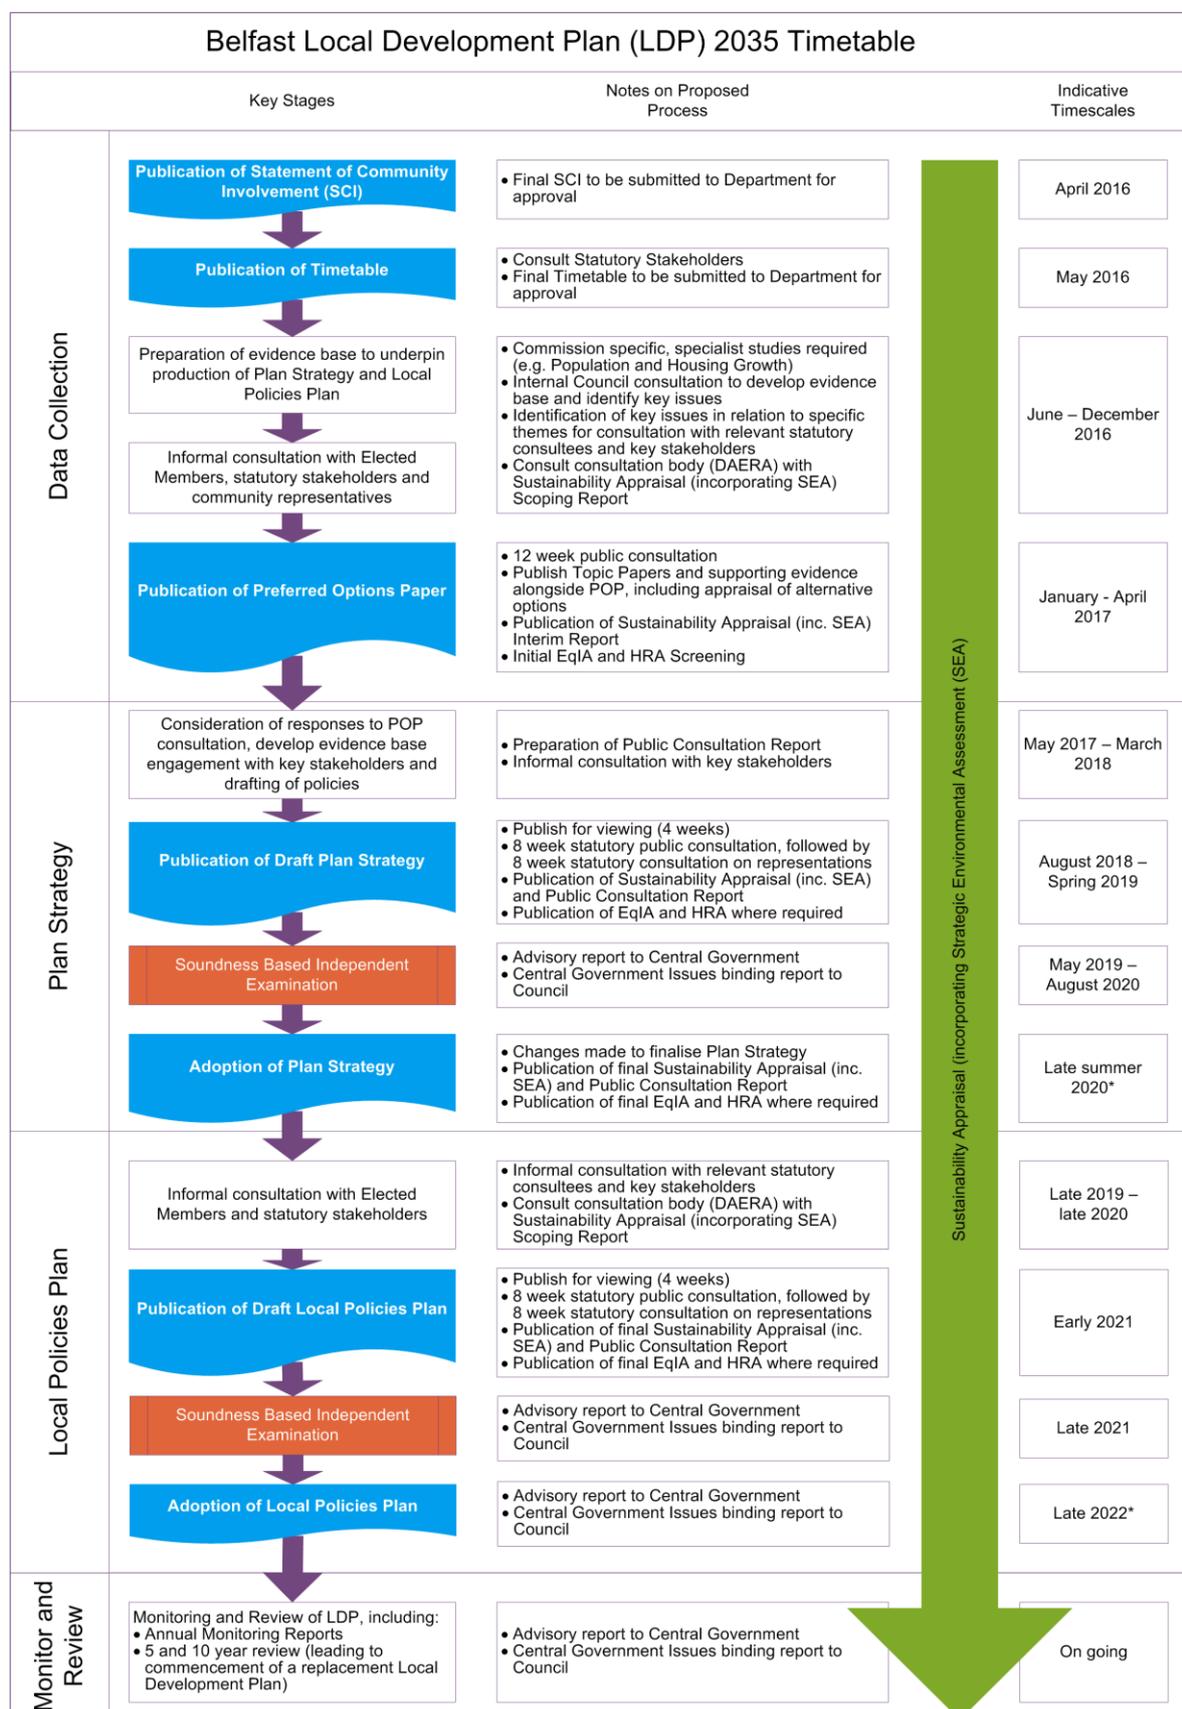

* May require a longer period depending on changes required following Independent Examination
